

12.BLOOD BANK MANAGEMENT- PES1UG24AM312 (Samyuktha V)

Added tasks necessary to backlog (ss- after moving some to sprint1)

Spaces / blood_bank_manager

BBM board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

More 2

Search backlog

Version

Epic

Quick filters

Backlog (5 work items)

2400

Create sprint

Create a whiteboard to plan your work

Try

☑ BBM-14 Handle load spikes

To Do

8

>

☑ BBM-13 Expiry flagging

To Do

5

<

☑ BBM-12 Donor response

To Do

5

=

☑ BBM-11 Eligibility check

To Do

3

=

☑ BBM-10 Donor registration

To Do

3

=

Created sprint 1

Spaces / [blood_bank_manager](#)

BBM board

Summary
 Timeline
 Active sprints
 Backlog
 Calendar
 List
 Forms
More 2 +

Version ▾

Epic ▾

Quick filters ▾

☐ ▾ **BBM Sprint 1**
 Add dates
(4 work items)

23 0 0

Start sprint

⋮

☒ BBM-6	Submit emergency request	To Do ▾	5		
☒ BBM-7	Match compatible donors	To Do ▾	8		
☒ BBM-8	Live inventory ledger	To Do ▾	5		
☒ BBM-9	Lock allocated bag	To Do ▾	5		

+ Create

≡

4 work items | Estimate: 23

Created sprint 2

Spaces / blood_bank_manager

BBM board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

More 2

Search backlog

Version

Epic

Quick filters

BBM Sprint 2

Add dates

(5 work items)

2400

BBM-10 Donor registration	To Do	3	=	
BBM-11 Eligibility check	To Do	3	=	
BBM-12 Donor response	To Do	5	=	
BBM-13 Expiry flagging	To Do	5	>	
BBM-14 Handle load spikes	To Do	8	<	

+ Create

Started sprint 1

BBM board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Search board

Version

Quick filters

Complete sprint

Group: Story

TO DO 4

Submit emergency request

BBM-6

5

IN PROGRESS

DONE

Submit emergency request

BBM-6

5

Match compatible donors

BBM-7

8

Live inventory ledger

BBM-8

5

Lock allocated bag

BBM-9

5

Spaces / blood_bank_manager

BBM board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Search board

Version

Quick filters

Complete sprint

Group: Story

TO DO 2

Live inventory ledger

BBM-8

5

Lock allocated bag

BBM-9

5

IN PROGRESS 2

Submit emergency request

BBM-6

5

Match compatible donors

BBM-7

8

DONE

Submit emergency request

BBM-6

5

Match compatible donors

BBM-7

8

TO DO 1

Lock allocated bag

BBM-9 5

+ Create

IN PROGRESS 1

Live inventory ledger

BBM-8 5

+ Create

DONE 2

Submit emergency request

BBM-6 5

Match compatible donors


BBM-7 8

Burndown chart sprint 1

Burndown Chart

How to read this chart

Track the total work remaining and project the likelihood of achieving the sprint goal. This helps your team manage its progress and respond accordingly.

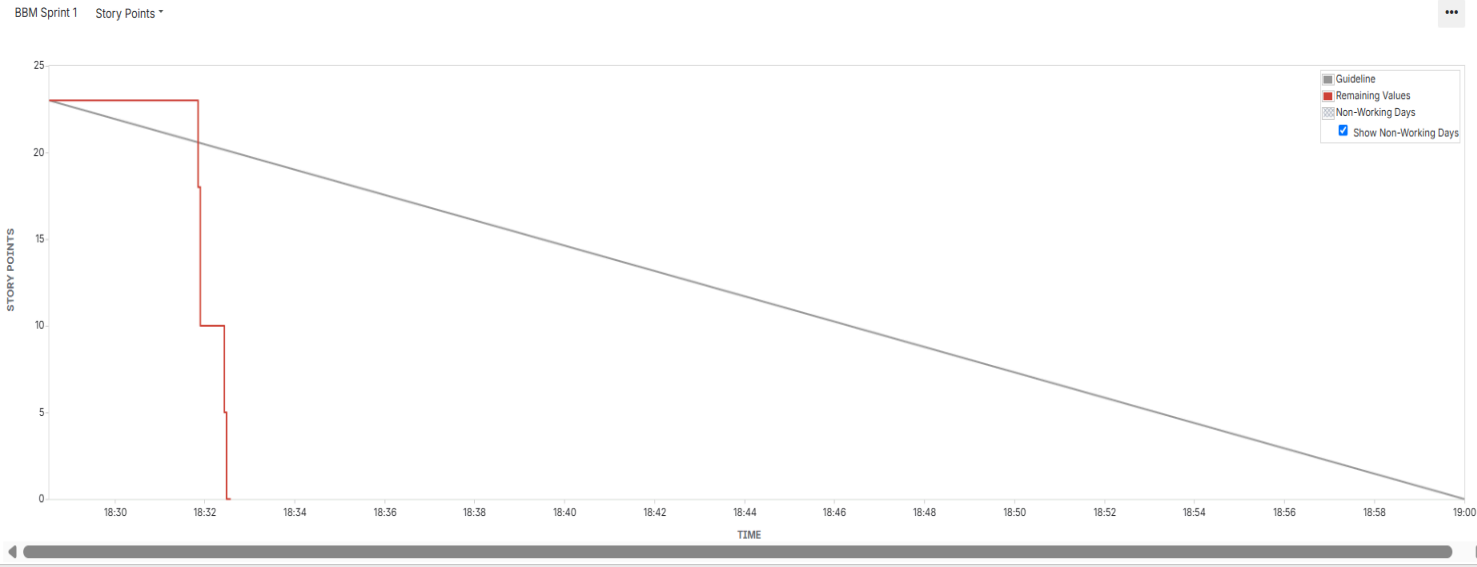

Date	Issue	Event Type	Event Detail	Story Points		
				Inc.	Dec.	Remaining
01/Sep/26 6:28 PM	BBM-6	Sprint start		5		
	BBM-7			8		
	BBM-8			5		
	BBM-9			5		
	Total					23
01/Sep/26 6:31 PM	BBM-6	Burndown	Issue completed	5		18
	BBM-7	Burndown	Issue completed	8		10
01/Sep/26 6:32 PM	BBM-8	Burndown	Issue completed	5		5
	BBM-9	Burndown	Issue completed	5		0
	BBM-6	Sprint ended by Samyuktha (PES1UG24AM312)				0
	BBM-7					0
	BBM-8					0
	BBM-9					0
	Total					0

Started sprint 2

Spaces / blood_bank_manager

BBM board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Reports

Search board

Version

Quick filters

Complete sprint

Group: Story

TO DO 5

Donor registration

BBM-10

3

Eligibility check

BBM-11

3

Donor response

BBM-12

5

Expiry flagging

BBM-13

5

Handle load spikes

BBM-14

8

Create

IN PROGRESS

DONE

Spaces / blood_bank_manager

BBM board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Reports

Search board

Version

Quick filters

Complete sprint

Group: Story

TO DO 3

Eligibility check

BBM-11

3

Expiry flagging

BBM-13

5

Handle load spikes

BBM-14

8

Create

IN PROGRESS 2

Donor registration

BBM-10

3

Donor response

BBM-12

5

DONE

Spaces / blood_bank_manager

BBM board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Reports

Search board

Version

Quick filters

Complete sprint

Group: Story

TO DO 1

Eligibility check

BBM-11

3

Create

IN PROGRESS 2

Handle load spikes

BBM-14

8

Expiry flagging

BBM-13

5

DONE 2

Donor registration

BBM-10


3

Donor response

BBM-12

5

Burndown chart sprint2

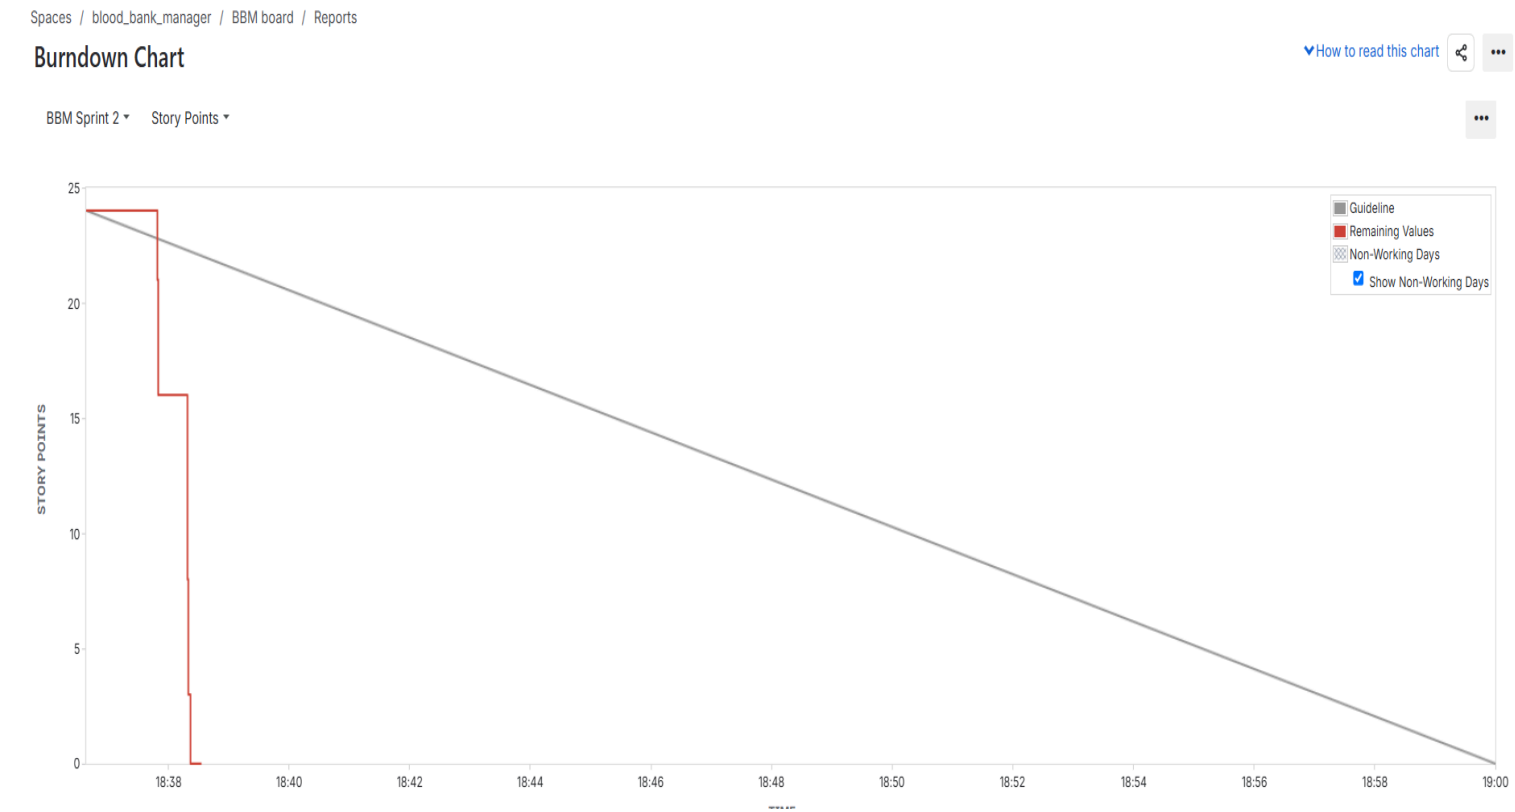

Spaces / blood_bank_manager / BBM board / Reports

Burndown Chart

▼How to read this chart

...

Date	Issue	Event Type	Event Detail	Story Points		
				Inc.	Dec.	Remaining
01/Sep/26 6:36 PM	BBM-10	Sprint start		3		
	BBM-11			3		
	BBM-12			5		
	BBM-13			5		
	BBM-14			8		
	Total					24
01/Sep/26 6:37 PM	BBM-10	Burndown	Issue completed	3		21
	BBM-12	Burndown	Issue completed	5		16
01/Sep/26 6:38 PM	BBM-14	Burndown	Issue completed	8		8
	BBM-13	Burndown	Issue completed	5		3
	BBM-11	Burndown	Issue completed	3		0
	BBM-10	Sprint ended by Samyuktha (PES1UG24AM312)				0
	BBM-11					0
	BBM-12					0
	BBM-13					0
	BBM-14					0
	Total					0

1. Did your estimations reflect the actual effort?

The Fibonacci-based estimates (1, 2, 3, 5, 8, 13, 20) were assigned based on the perceived complexity, technical risk, and scope of each user story. Higher-complexity stories such as "Match compatible donors" (8 points), which required cross-referencing inventory, geolocation, and donor eligibility simultaneously, were weighted appropriately against simpler stories such as "Donor registration" (3 points). As this exercise simulated the sprint process without full implementation, the estimates could not be validated against actual development time; however, the relative sizing between stories was internally consistent and reflected a logical assessment of complexity.

2. Was your backlog well-prioritized?

The backlog prioritization followed a risk- and value-based approach. Stories directly supporting the system's core objective — emergency blood matching and real-time inventory management (FR-001, FR-002) — were assigned

High priority, as these represent the minimum viable functionality of the system. Donor registration and eligibility verification were assigned Medium priority, as they are necessary supporting functions but not part of the critical path. The scalability requirement (handling 20x load during mass-casualty events) was assigned Low priority, as it is a robustness enhancement rather than a blocker for core functionality within the scope of this project.

3. How did your simulated sprint align with your plan?

The sprint plan closely followed the intended structure. Sprint 1 was scoped to deliver the core request-to-match workflow — request submission, donor matching, inventory tracking, and allocation locking — totaling 23 story points. Sprint 2 was scoped to build on this foundation with donor-facing functionality and system safeguards — registration, eligibility checks, donor response handling, expiry flagging, and scalability — totaling 24 story points. This sequencing ensured that Sprint 1 delivered an end-to-end usable core, with Sprint 2 extending rather than duplicating that functionality.

4. What insights did the burndown chart give about your team's capacity?

As this sprint was simulated individually rather than executed by a distributed team over real time, the burndown chart primarily reflects the order in which stories were marked complete rather than actual team velocity or capacity. In a real-world Scrum context, a steadily declining burndown line would indicate consistent progress across the sprint, whereas a chart that remains flat before a sharp late decline would suggest work being concentrated near the deadline. This distinction would be a key indicator of a team's actual pacing and capacity planning.
